

U.S. Army Corps of Engineers Wilmington District

Ongoing & Upcoming Contracts




US Army Corps of Engineers
BUILDING STRONG®





<p>Morehead City Harbor Inner Harbor FY '11 Map Date: Oct 7, 2011 Scale: 1:50,000 Dredging and Placement Notes are incorporated.</p>	Project:	Morehead City Harbor Inner Harbor
	Dredging Depth:	35 & 45 ft (required); + 2 ft
	Dredging Width:	700 - 1500 ft
	Dredging Length:	Varies
	Dredging Quantity:	~478,000 cubic yards
	Material Type:	Sand
	Placement Area:	Nearshore & ODMDS
	Distance to Place Area:	2 - 5 miles
	Type of Equipment:	Mechanical
	Env. Window:	August 1 - March 31
	Reason for Window:	Fisheries
	Est. Start Date:	July 15, 2011
	Est. Completion Date:	October 5, 2011
Contract Completion:	November 12, 2011	
Contract Amount:	~\$3,800,000	
Contractor:	Norfolk Dredging	



BUILDING STRONG®

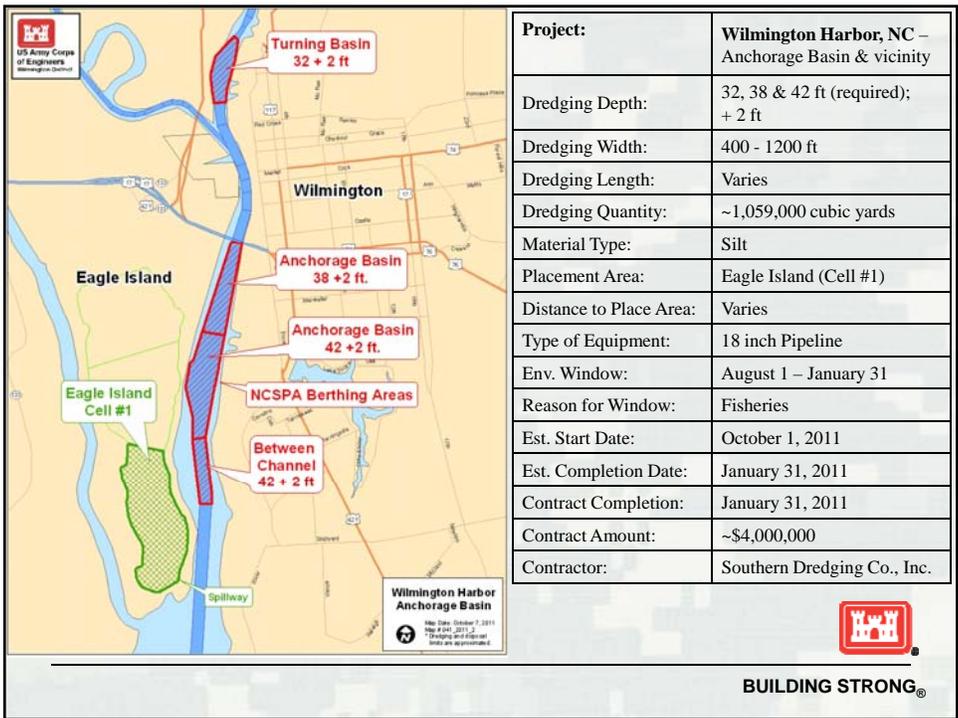



Project:	Wilmington Harbor, NC – Eagle Island Improvements
Services:	<ul style="list-style-type: none"> - Cell #2 Spillway Replacements - Cell #2 Dike Raise - Cell #3 Spillway Replacements - Cell #3 Dike Repair
Est. Start Date:	October 30, 2011
Est. Completion Date:	Unknown
Contract Completion:	Unknown
Contract Amount:	~\$5,300,000
Contractor:	Corey Enterprises

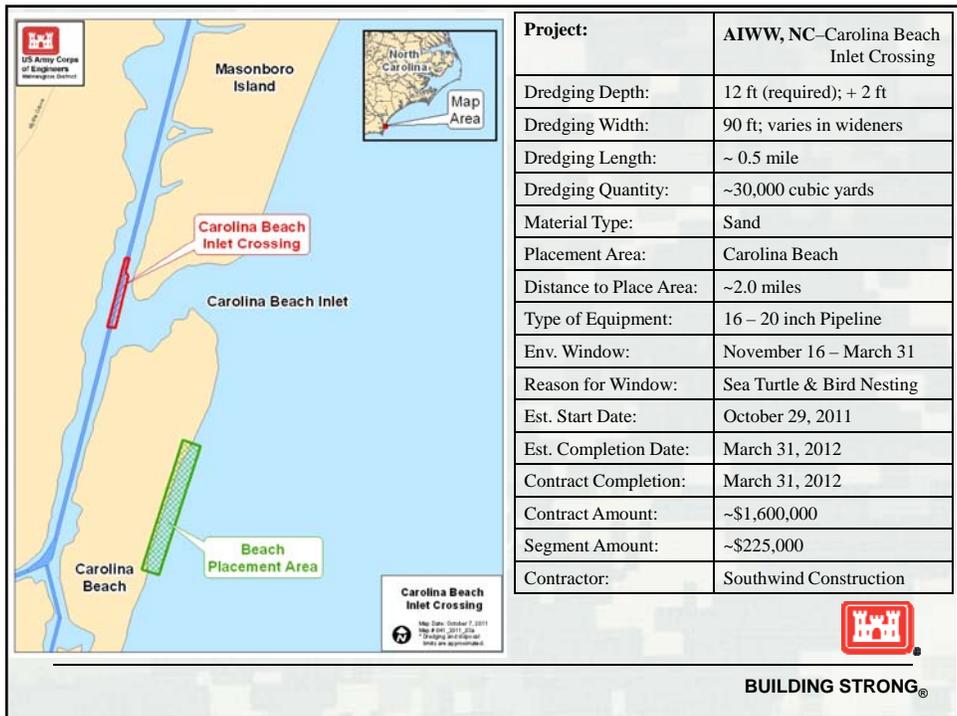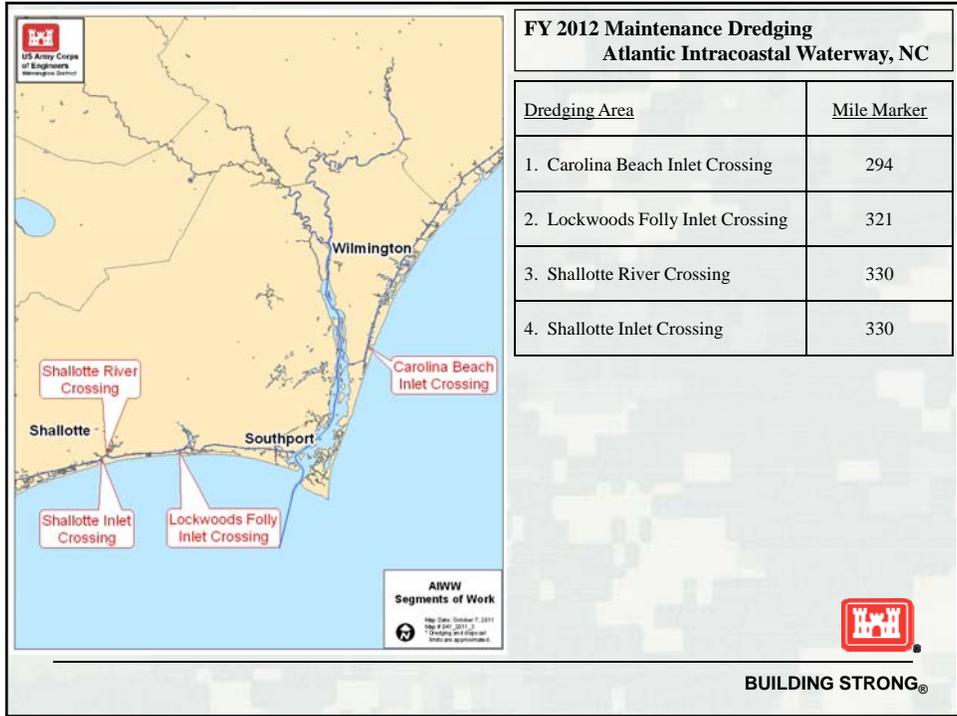

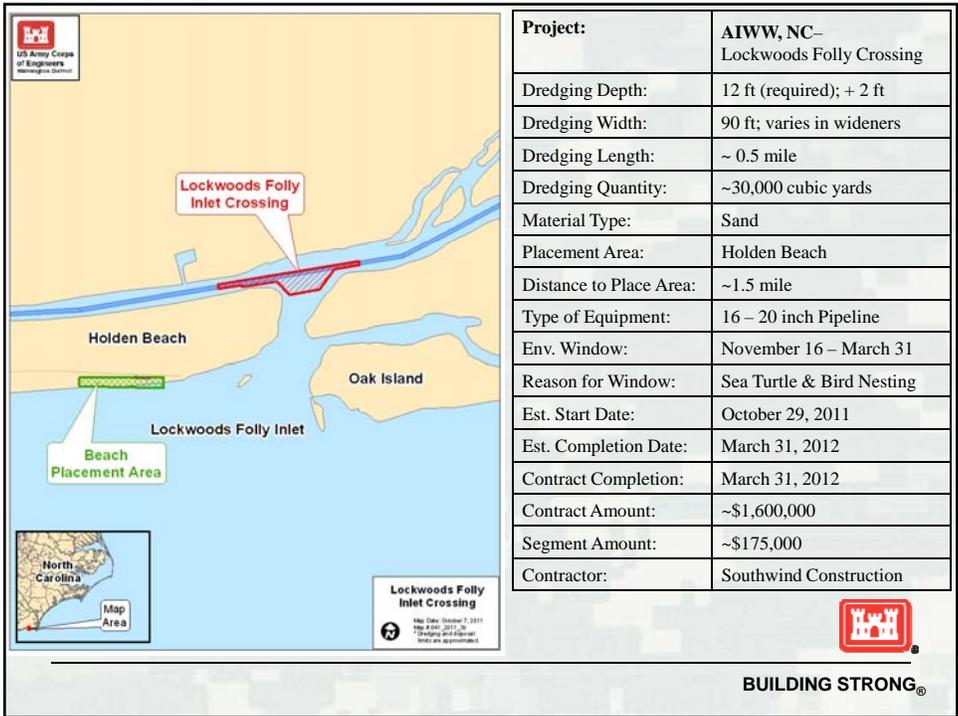





Project:	AIWW, NC – Shallotte River Crossing
Dredging Depth:	12 ft (required); + 2 ft
Dredging Width:	90 ft; varies in wideners
Dredging Length:	~ 0.3 mile
Dredging Quantity:	~35,000 cubic yards
Material Type:	Sand
Placement Area:	DA 300
Distance to Place Area:	~0.5 mile
Type of Equipment:	16 – 20 inch Pipeline
Env. Window:	November 16 – March 31
Reason for Window:	Sea Turtle & Bird Nesting
Est. Start Date:	October 29, 2011
Est. Completion Date:	March 31, 2012
Contract Completion:	March 31, 2012
Contract Amount:	~\$1,600,000
Segment Amount:	~\$180,000
Contractor:	Southwind Construction

Shallotte River and Inlet Crossings
 Map Date: October 7, 2011
 Map # 101_2011_01
 Changes and Additions:
 None are implemented.

BUILDING STRONG®

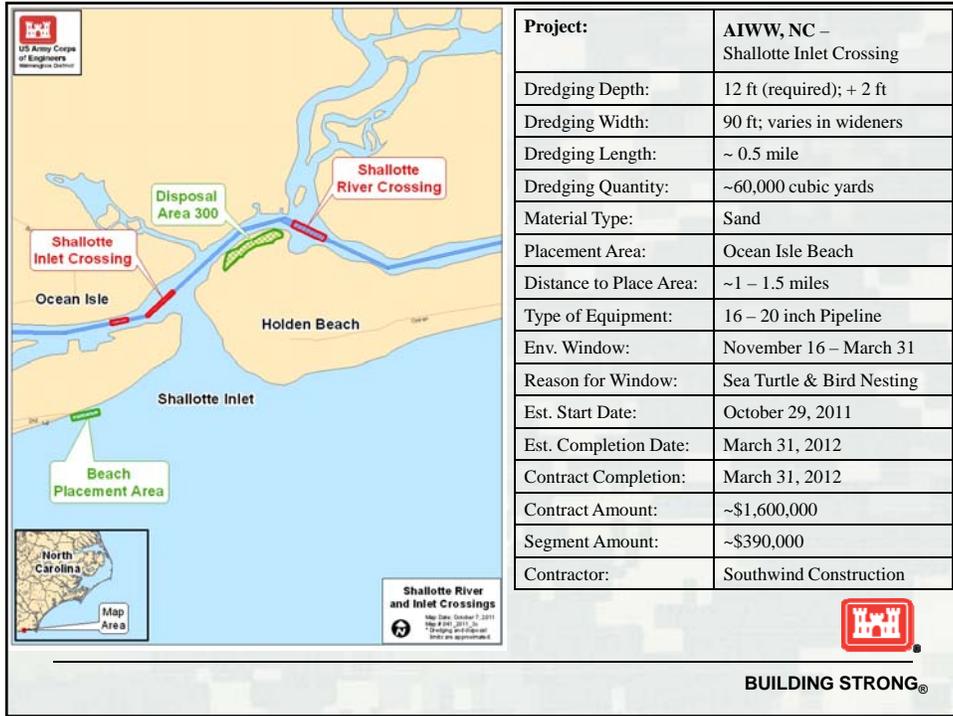


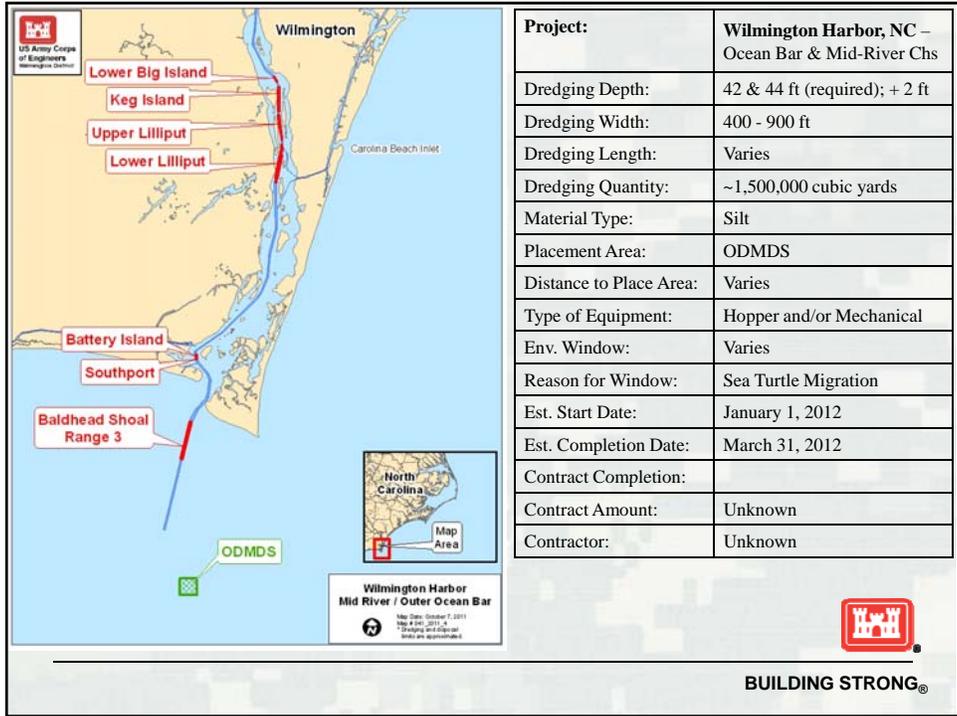

Project:	Wilmington Harbor, NC – Ocean Bar & Mid-River Chs
Dredging Depth:	42 & 44 ft (required); + 2 ft
Dredging Width:	400 - 900 ft
Dredging Length:	Varies
Dredging Quantity:	~1,500,000 cubic yards
Material Type:	Silt
Placement Area:	ODMDS
Distance to Place Area:	Varies
Type of Equipment:	Hopper and/or Mechanical
Env. Window:	Varies
Reason for Window:	Sea Turtle Migration
Est. Start Date:	January 1, 2012
Est. Completion Date:	March 31, 2012
Contract Completion:	
Contract Amount:	Unknown
Contractor:	Unknown



BUILDING STRONG®

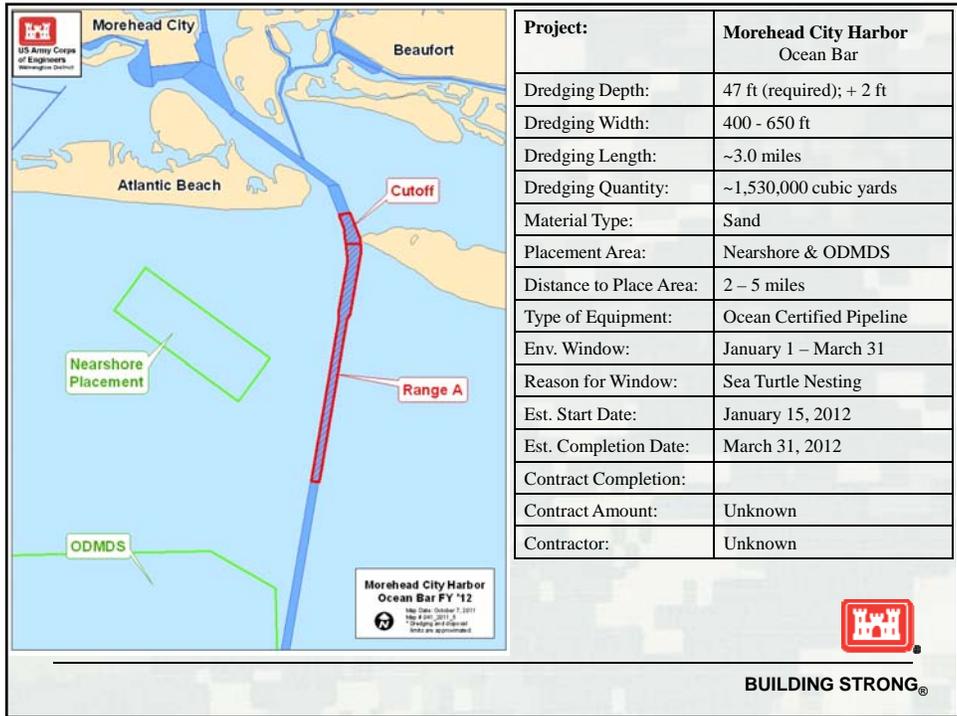

Project:	Morehead City Harbor Ocean Bar
Dredging Depth:	47 ft (required); + 2 ft
Dredging Width:	400 - 650 ft
Dredging Length:	~3.0 miles
Dredging Quantity:	~1,530,000 cubic yards
Material Type:	Sand
Placement Area:	Nearshore & ODMDS
Distance to Place Area:	2 – 5 miles
Type of Equipment:	Ocean Certified Pipeline
Env. Window:	January 1 – March 31
Reason for Window:	Sea Turtle Nesting
Est. Start Date:	January 15, 2012
Est. Completion Date:	March 31, 2012
Contract Completion:	
Contract Amount:	Unknown
Contractor:	Unknown



BUILDING STRONG®



Wilmington District Points of Contact

Roger Bullock

(910) 251-4822

roger.d.bullock@usace.army.mil

Bob Keistler

(910) 251-4709

robert.w.keistler@usace.army.mil



BUILDING STRONG®
