



US Army Corps of Engineers  
New England District




# New England District FY 2010 Dredging Program




**US Army Corps of Engineers**  
New England District

BUILDING STRONG™

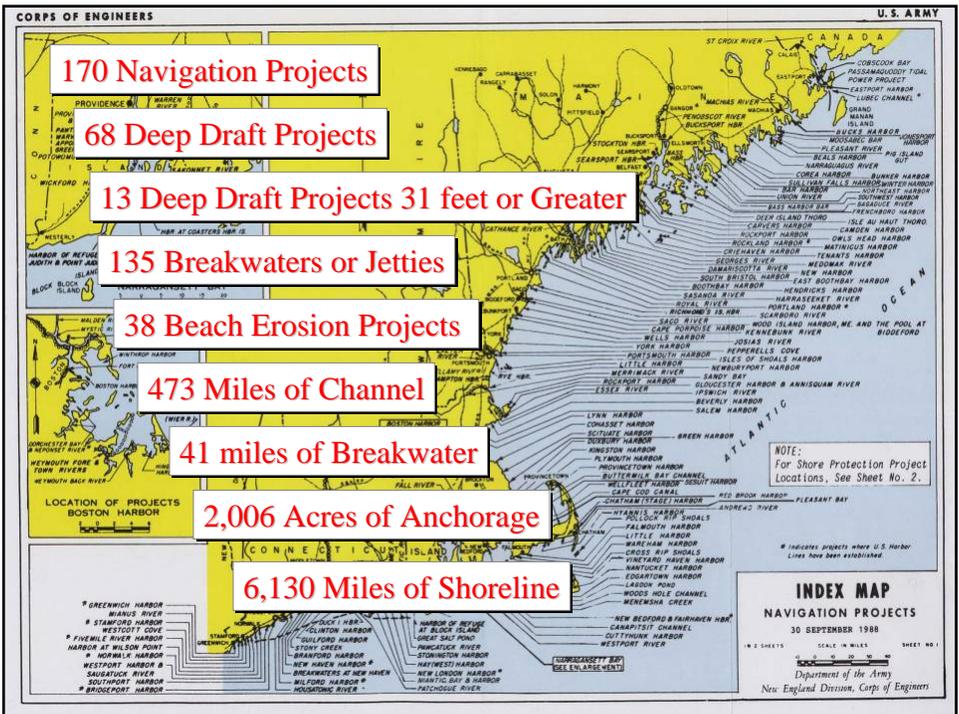



# US Army Corps of Engineers New England District



## Schedule For FY-10 O&M Dredging Work for New England District North Atlantic Division

|    |   | NAE O&M and New Work Dredging Program |     |     |     |     |     |     |     |     |     |     |     |     |     |
|----|---|---------------------------------------|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|-----|
|    |   | FY 10                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    |   | SEP                                   | OCT | NOV | DEC | JAN | FEB | MAR | APR | MAY | JUN | JUL | AUG | SEP | OCT |
| 1  | Bass Harbor, ME<br>Bucket                 | TBD                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 60 KCY                                    | IFB                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 2  | Boston Harbor Rock Removal, MA<br>Bucket  | TBD                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 3 KCY                                     | IFB                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 3  | Cape Cod Canal<br>Hopper                  | Great Lakes Dredge & Dock             |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 25 KCY                                    | AWARD                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 4  | Bullock's Cove, RI<br>Bucket              | Village Dock, Inc                     |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 50 KCY                                    | AWARD                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 5  | Green Harbor, MA<br>Bucket                | Cashman Dredging & Marine Cont.       |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 60 KCY                                    | AWARD                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 6  | Narragansett River, ME<br>Bucket          | Prock Marine Co                       |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 60 KCY                                    | AWARD                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 7  | Newburyport Harbor, MA<br>Hopper/Pipeline | TBD                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 160 KCY                                   | IFB                                   |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 8  | Point Judith, RI<br>Bucket                | Village Dock, Inc                     |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 30 KCY                                    | AWARD                                 |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 9  | Aunt Lydia's Cove, MA<br>Government       | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 30 KCY                                    | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 10 | Great Salt Pond, RI<br>Government         | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 30 KCY                                    | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |
| 11 | Andrews River, MA<br>Government           | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |
|    | 15 KCY                                    | NA                                    |     |     |     |     |     |     |     |     |     |     |     |     |     |

BUILDING STRONG™

3




# US Army Corps of Engineers New England District



## Newburyport Harbor

Entrance Channel Dredging  
 Project Depth: 16' MLLW  
 Last Dredged: 1999  
 Quantity: 160,000 cy  
 Material Type: Sand  
 Equipment Type: Hopper/Cutter dredge  
 Disposal Site: Beach  
 Pump Distance: 1 mile

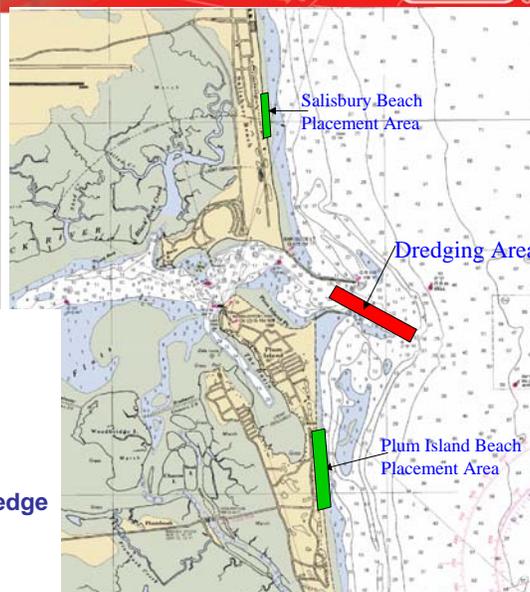

BUILDING STRONG™

